PROJECT MANPOWER

Coworking Space Management Software — Cobi

> **Project**: Coworking Space Operations Management System
> **Client**: Cobi
> **Date**: 18/04/2026
> **Version**: 1.0

---

1. Manpower Overview

Phase	Duration	Headcount	Platform
Phase 1 — Core Operations	5 months	**6 people**	🖥️ Web App
Phase 2 — Expansion & Mobile	3 months	**4 people**	📱 Mobile + Web

Phase	Duration	Headcount	Platform
Phase 3 — Advanced & Finalization	2 months	**2.5 people**	🖥️ Web App

---

2. Phase 1: Core Operations (6 people — 5 months)

Team Composition

#	Role	Qty	Duration	Key Responsibilities
1	**Project Manager**	1	Full-time 5 months	Project management, Cobi communication, progress tracking, Scrum Master
2	**Business Analyst**	0.5	Part-time 5 months	Detailed requirements, specs writing, UAT support
3	**Backend Developer (Senior)**	1	Full-time 5 months	DB design (40+ entities), API architecture, payment gateway integration
4	**Backend Developer (Mid)**	1	Full-time 5 months	API development, business logic, unit tests
5	**Frontend Developer (Senior)**	1	Full-time 5 months	Complete UI, API integration (prototype 95% ready)

#	Role	Qty	Duration	Key Responsibilities
6	**QA/Tester**	1	Full-time 5 months	Test plan, manual + automation testing, regression
7	**DevOps**	0.5	Part-time 5 months	CI/CD, Docker, monitoring, infrastructure

Phase 1 Staffing Chart

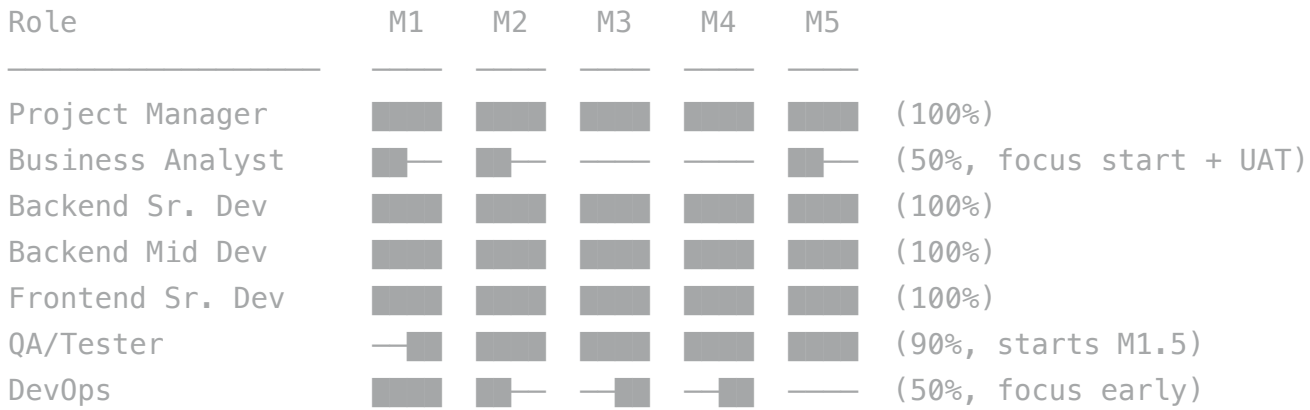

Sprint Assignments

Sprint	Week	Backend Sr.	Backend Mid	Frontend Sr.	QA
S0 Kickoff	1-2	DB Design, API conventions	Setup project, seed data	FE API layer setup	Test plan
S1-2 Foundation	3-6	Auth API, RBAC	Property API (CRUD)	Integrate Auth + Property	Test Auth flows
S3-4 Customer	7-10	Customer API (3 types)	Pricing engine	Integrate Customer + Pricing	Test Customer + Pricing
S5-7 Booking	11-16	Booking + Contract API	Payment integration	Integrate Booking + Contract + Payment	Test E2E flows
S8-9 Support	17-18	Dashboard APIs	Credit + Inventory	Dashboard + Portal	Regression testing
S10 UAT	19-20	Bug fix, performance	Bug fix, migration	Bug fix, polish	UAT coordination

---

3. Phase 2: Expansion & Mobile (4 people — 3 months)

Team Composition

#	Role	Qty	Duration	Key Responsibilities
1	**Project Manager**	1	Full-time 3 months	Project management, continued Cobi communication
2	**Backend Developer (Fullstack)**	1	Full-time 3 months	API for mobile + new web modules (CRM, Events)
3	**Mobile Developer**	1	Full-time 3 months	React Native / Flutter — tenant iOS & Android app
4	**QA/Tester**	1	Full-time 3 months	Web + mobile app testing, regression

Phase 2 Staffing Chart

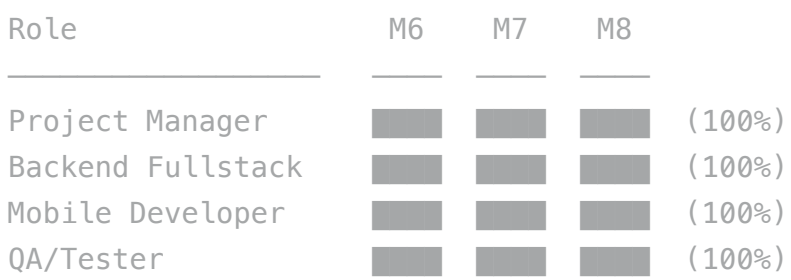

> 📱 **Mobile App is for tenants only**. Admin/staff use the Web App.

Sprint Assignments

Sprint	Backend Fullstack	Mobile Developer	QA
S11-12	Mobile API endpoints	App skeleton, Auth, Booking UI	Test mobile flows
S13-14	CRM + Access Control API	Payment, QR check-in, Push	Test CRM + mobile
S15-16	Events + Feedback API	Polish, submit to stores	UAT mobile + web

---

4. Phase 3: Advanced & Finalization (2.5 people — 2 months)

Team Composition

#	Role	Qty	Duration	Key Responsibilities
1	**Backend Developer**	1	Full-time 2 months	Advanced reports, Staff API, Portal API
2	**Frontend Developer**	1	Full-time 2 months	Reports UI, Staff UI, Portal, i18n polish

#	Role	Qty	Duration	Key Responsibilities
3	**QA/Tester**	0.5	Part-time 2 months	Regression, final UAT

Phase 3 Staffing Chart



---

5. Project-wide Manpower Summary

5.1 Headcount by Phase

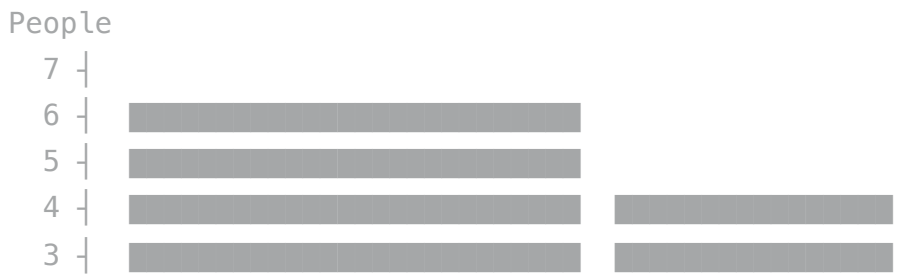

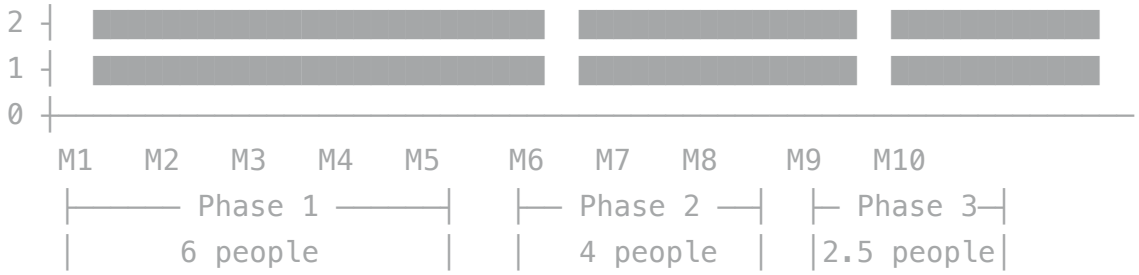

5.2 Total Man-months

Role	Phase 1	Phase 2	Phase 3	**Total (man-months)**
Project Manager	5	3	—	**8**
Business Analyst	2.5	—	—	**2.5**
Backend Sr. Developer	5	—	—	**5**
Backend Mid/Fullstack	5	3	2	**10**
Frontend Sr. Developer	5	—	2	**7**
Mobile Developer	—	3	—	**3**
QA/Tester	5	3	1	**9**
DevOps	2.5	—	—	**2.5**

Role	Phase 1	Phase 2	Phase 3	**Total (man-months)**
TOTAL	**30**	**12**	**5**	**47 man-months**

---

6. Skill Requirements

Role	Key Skills	Experience
Project Manager	Agile/Scrum, stakeholder management, IT project delivery	3+ years PM
Business Analyst	Requirements analysis, wireframes, acceptance criteria	2+ years BA
Backend Sr. Developer	NestJS, PostgreSQL, Redis, Payment gateways (VNPay, MoMo)	4+ years Backend
Backend Mid Developer	NestJS/Node.js, TypeORM/Prisma, REST API	2+ years Backend
Frontend Sr. Developer	React 19, TypeScript, TanStack Query, Tailwind CSS	3+ years Frontend
Mobile Developer	React Native or Flutter, mobile payments, push notifications	2+ years Mobile
QA/Tester	Manual + automation testing, API testing, mobile testing	2+ years QA
DevOps	Docker, CI/CD (GitHub Actions), AWS/VPS, monitoring	2+ years DevOps

---

7. Team Strengths

Advantage	Details
🎯 **Ready Prototype**	Frontend 95% complete → Frontend Sr. focuses on API integration instead of building from scratch
🔧 **Fullstack Capability**	Backend Mid can flexibly support frontend when needed
📱 **Dedicated Mobile**	Mobile Dev specialized in React Native/Flutter, not shared with web
🧪 **Early QA**	QA participates from Sprint 1, writes test plan in parallel with development
📋 **Regular Demos**	PM organizes bi-weekly demos, Cobi always stays informed

---

8. Quality Commitment

- **Code Review**: All code reviewed by Senior before merging
- **Automation Testing**: Unit tests + integration tests for APIs
- **QA Testing**: Manual + regression testing every sprint
- **UAT**: Cobi acceptance testing before each go-live

- **Warranty**: 6 months free bug fixes after each Phase go-live
